"Home Plate" Panorama, Spirit Rover, Gusev Crater

NASA/JPL/Cornell

Science Committee report to the NASA Advisory Council April 17, 2008

AS15-M-2087 (Moon)

Mars HST

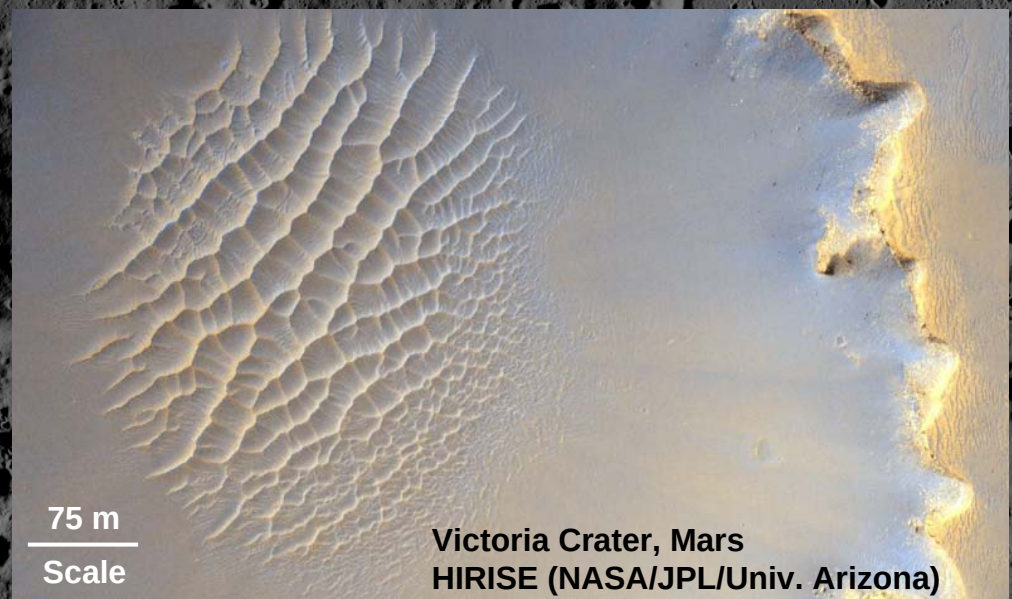

75 m Scale

Victoria Crater, Mars
HIRISE (NASA/JPL/Univ. Arizona)

Highlights in SMD

- Increases in 2008 and 2009 for R&A programs in Astrobiology and in Lunar Science, and strong program of R&A across the board (Astrophysics, Heliophysics, Planetary Science).
- Stand-Alone Mission of Opportunity Notification (SALMON), with a first release in May 2008 and annual releases thereafter.
- JWST passed Preliminary Design Review (PDR) with no major issues identified; Non-Advocate Review (NAR) this week
- Mars Phoenix Scout mission en route to Mars with landing May 25
- MESSENGER on the way to a second encounter with Mercury on Oct 6

FY09 Program Changes

- Earth Science:
  - $600M over 5 years for new Decadal missions
  - Soil Moisture Active/Passive (SMAP) and IceSat II (2012, 2015 launches)
- Astrophysics: Joint Dark Energy Mission (JDEM) (launch in 2014)
- Heliophysics: Solar Probe Plus (launch in 2015)
- Planetary:
  - Outer Planets Flagship (launch in 2016/2017)
  - Lunar science orbiter, LADEE (launch in 2010/2011)
  - International Lunar Network (planning for FY12-FY14)

Changes represent good use of efficiencies, out-year mission Ops Savings, and re-phasings for several missions.

Meeting Focus

- The SC's focus in this meeting was on NASA's Planetary Science portfolio:
  - FY09 President's Budget discussion
  - Status of Outer Planets Flagship mission concept studies
  - Plans for next New Frontiers and Discovery opportunities
  - Mars Science Laboratory Status
  - Mars Sample Return planning
- Briefings by:
  - James Green, Director Planetary Science Division
  - Doug McCuistion, Director Mars Exploration Program
  - In attendance: Chuck Gay / SMD's new Deputy AA
- Other Briefings:
  - Strategic Review of Expendable Launch Vehicle Options (with Space Ops); presentation by Bill Wroebel
  - Lunar Rover Trades and Status (with Exploration & Space Ops) – M. Gernhardt

Planetary Science Portfolio

- The Planetary Science portfolio is well balanced along some key dimensions:
  - Good mix of small, medium and large missions
  - Good mix of strategic and competed, PI-led missions
  - Programs exist that provide opportunities extending to the full range of solar system targets (but not all at once!)
- Mars is the focus of a sustained campaign of scientific exploration
  - Continued need to integrate Mars intellectually with the rest of Planetary Science; next NRC decadal survey (to start up in 2009) will help
  - Mars Sample Return remains the goal; promises largest leap in understanding after MSL
  - Mars budget took a significant reduction in the FY09 request vis-à-vis the FY08 request

Lunar Science Program to Complement US Space Exploration Policy

- The Lunar Science “Full Moon” Program complements the Lunar Exploration Architecture.
  - Provides robotic science precursor missions.
  - Supports training of next generation of scientists for lunar program.
- SMD has initiated plans to implement a NASA Lunar Science Institute (administered through Ames), with distributed nodes to be established through a competitive proposal process.
  - Themes include exploration as well as science.
  - ESMD support of one or two nodes would be appropriate.
- OSEWG (NASA) and LEAG (NAC, stakeholder communities) working to develop science and exploration roadmap that is consistent and integrated with the exploration architecture.

Lunar Missions Schedule

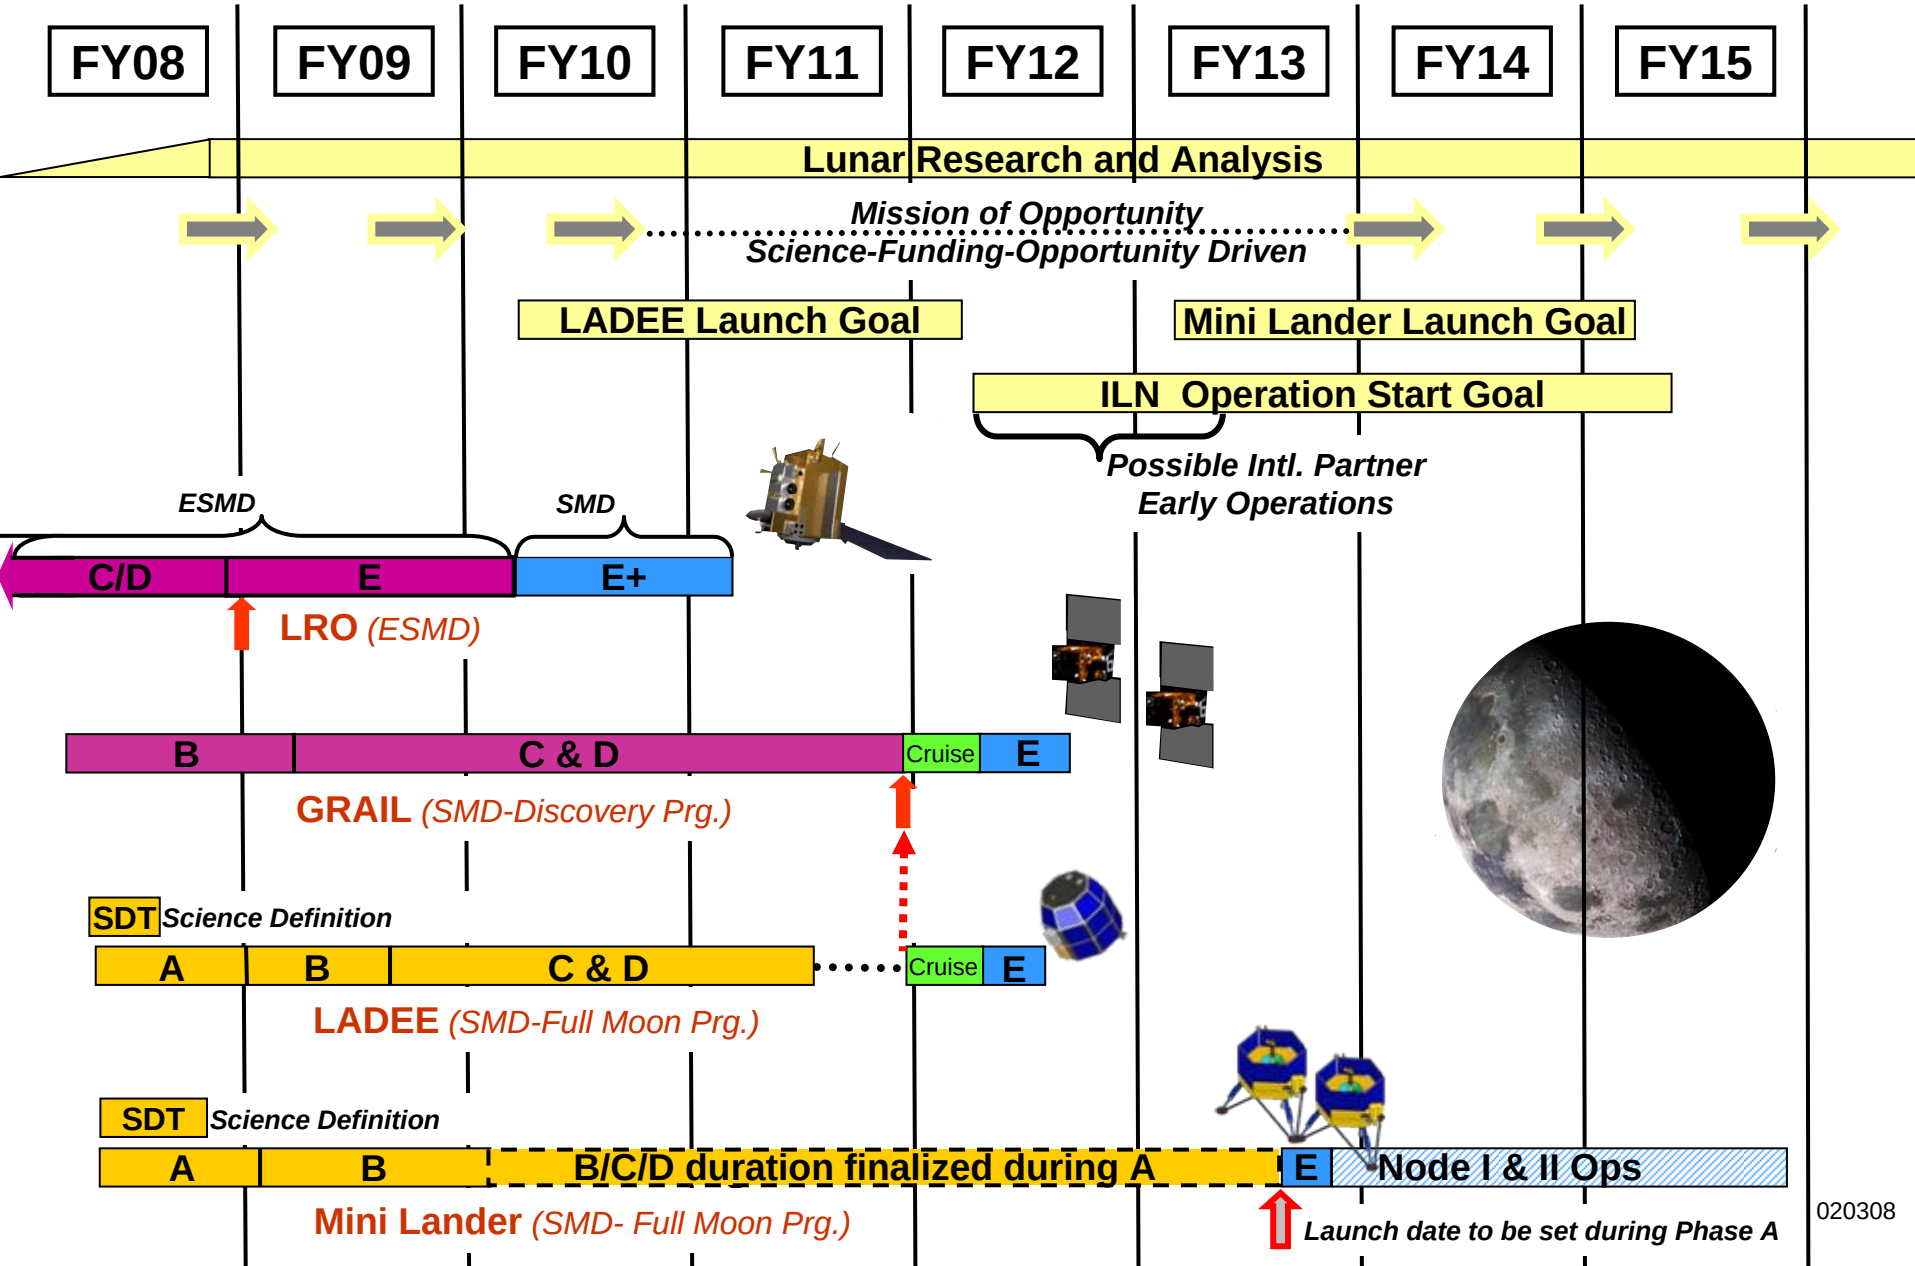

020308

Planetary Science Portfolio Challenge

- FY09 includes both an Outer Planets Flagship (2017) and Mars Sample Return (2018/2020) as new programs
- However, out-year profile makes it highly unlikely both can be done at the same time -- NASA needs to work this over the next few budget cycles
- Both missions require - and will benefit greatly from - international collaboration

Outer Planets Flagship Mission Studies

Europa - NASA lead

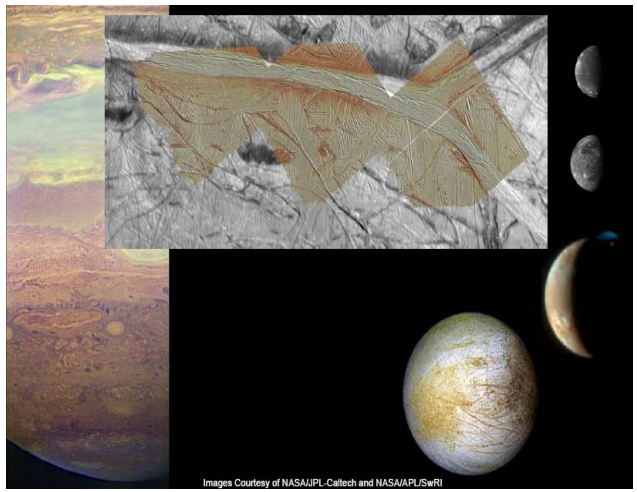

Jupiter System - ESA lead

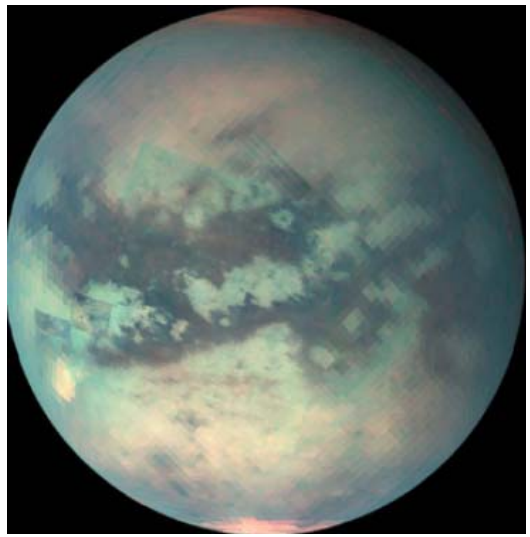

Titan - NASA lead

- Outer Planet Mission program characteristics:
  - Focused missions (not like Cassini, Galileo)
  - Europa Jupiter System Mission (EJSM) consisting of NASA Europa Orbiter, ESA Jupiter Planetary Orbiter, JAXA Magnetospheric Orbiter
  - Titan Saturn System Mission (TSSM) consisting of NASA Titan Orbiter, ESA *in situ* vehicles (lander & balloon)
  - NASA cost cap ($2.1B FY07), MMRTGs only, 34m DSN

Mars Exploration Program

- Work on the Mars exploration architecture is focused on optimizing the mix and timing of missions to meet the highest priorities of the scientific community.

- The planetary science community, through NRC, MEPAG, and the NAC Planetary Science Subcommittee, supports Mars Sample Return (MSR) as a goal, and supports plans to enable the launch of an MSR mission or missions the 2018-2020 timeframe as long as it can be done capably and at cost that is not detrimental to the overall Mars Exploration and Planetary Science programs.

Mars Exploration Program

- Ongoing planning, including budgetary and cost considerations, of the Mars Exploration Architecture for Mars Sample Return is proceeding well.
  - MEPAG Feb. ’08; Mars Architecture Tiger Team (Feb and Apr ’08)
  - Includes focused efforts to make and incorporate realistic estimates of associated costs and risks into architecture planning.

- Because of cost and scope, international partnerships are necessary for MSR
  - NASA has begun efforts to coordinate such partnerships through the IMARS (International Mars Architecture for the Return of Samples).

Mars Sample Return (3-launch Scenario)

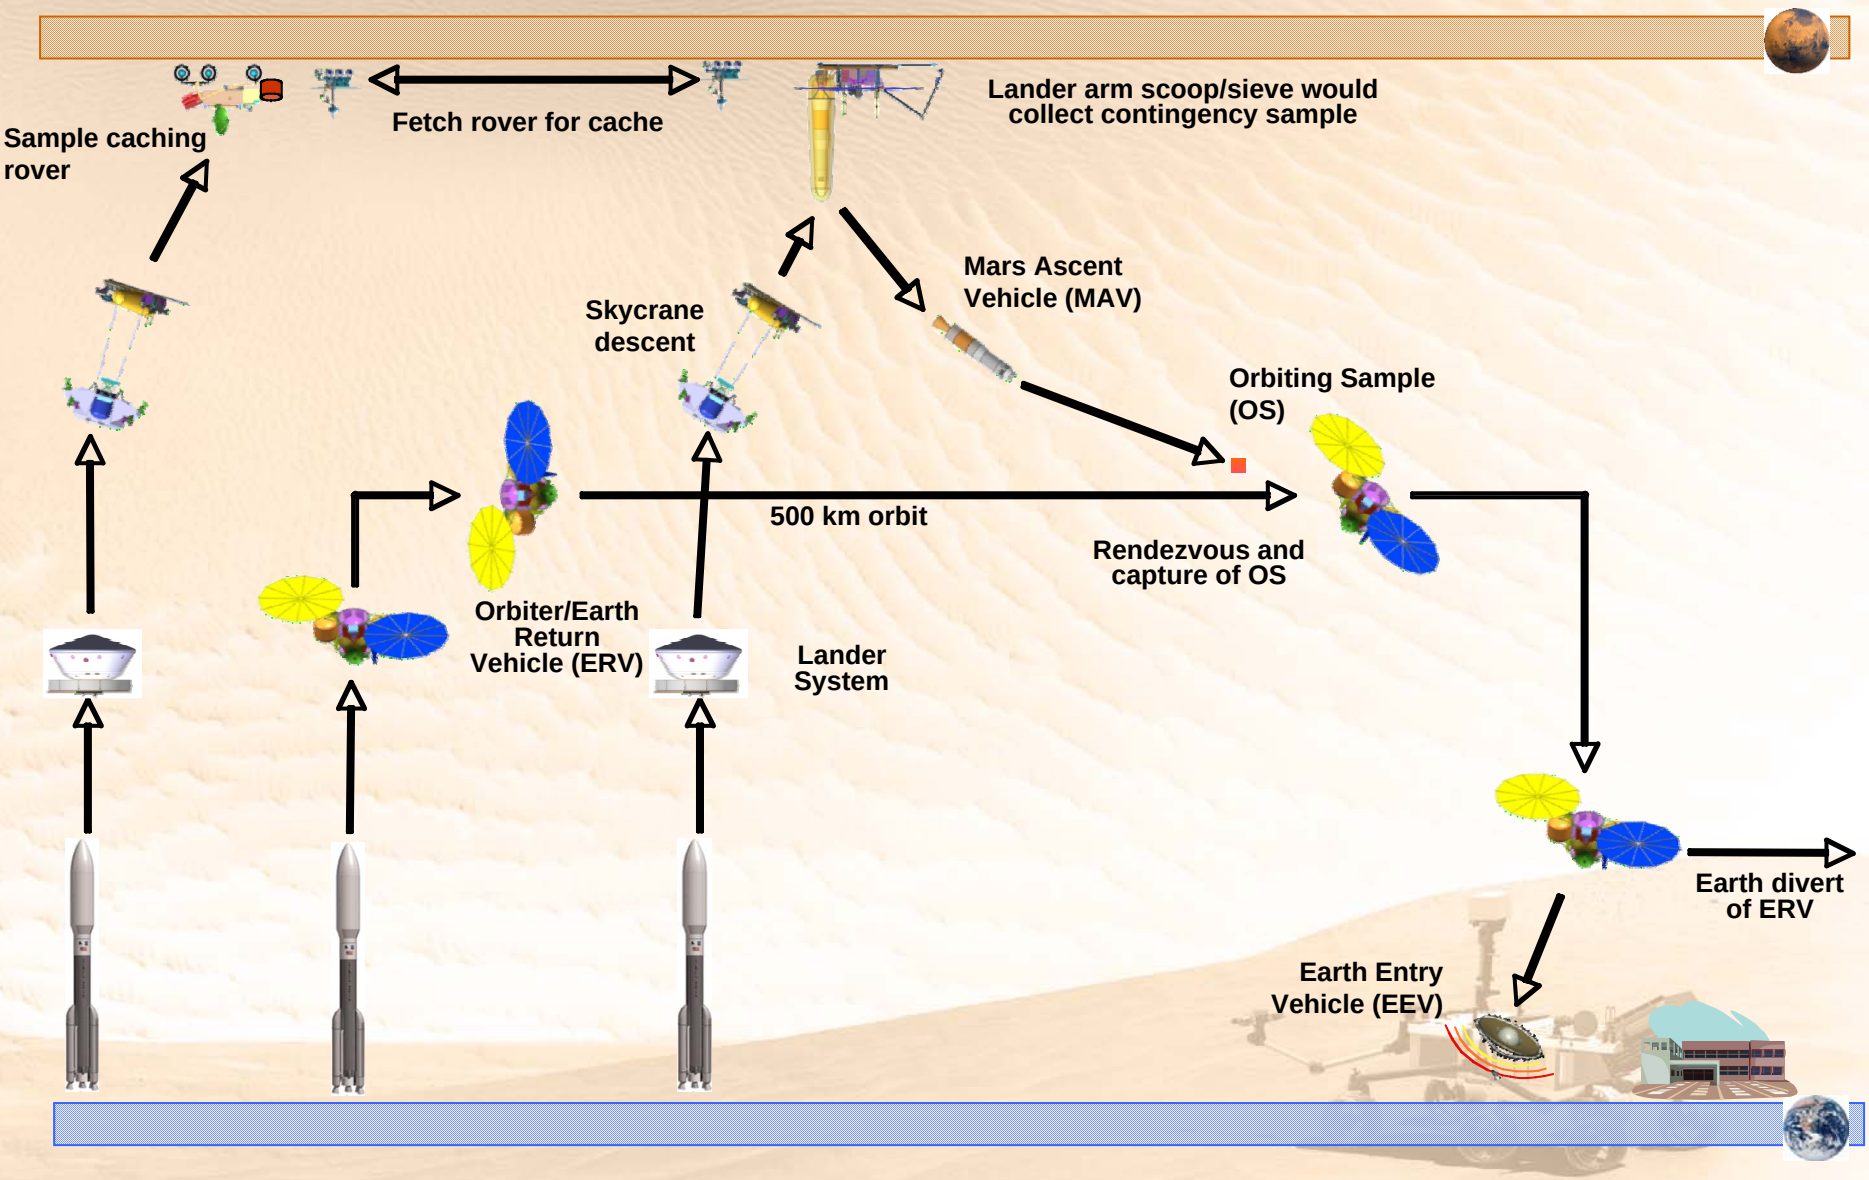

Mars Science Laboratory (MSL)

- Cost growth in the MSL Project remains a concern within the Mars Exploration Program and the Planetary Science Division.
- The Mars program recently investigated the consequences of a launch slip from 2009 to 2011 if required by schedule pressures.
- The additional cost of slipping the launch, however, could be as high as $350M. Given the cost of a delayed launch, it will be more efficient to solve MSL's cost growth problems in 2008 and 2009 so that the mission can remain on schedule for a 2009 launch.
- MSL is not only a key mission for the Mars Program, but also has priority at the Agency level.

Mars Science Laboratory

Short Title of Recommendation

- Launch the Mars Science Laboratory in 2009

Brief Description of Recommendation:

- NASA should continue to make every effort toward MSL mission success with a launch in 2009. NASA should continue to recognize MSL as an Agency-wide priority, and the Agency should assist the program in finding the resources necessary for mission success

Background - Long-lived Power Sources

- For many planetary mission concepts, solar / battery power is insufficient for long-term power supply or sustainability through operation at extremely low temperatures.
- Development of the Advanced Stirling Radioisotope Generator increases greatly the efficiency of usage of radioisotope fuel and is a positive step, but an adequate supply of Pu(238) is also important.
- An immediate beneficiary of such development would be the International Lunar Network landers, but such power supplies would benefit other missions including a Mars surface network and missions to the outer planets.

Advanced Stirling Radioisotope Generator Engineering Unit

- Operation in space and on surface of atmosphere-bearing planets and moons
- Characteristics:
  - ≥14 year lifetime
  - Nominal power : 140 We
  - Mass ~ 20 kg
  - System efficiency: ~ 30 %
  - 2 GPHS ("Pu^{238} Bricks") modules
  - Uses 0.8 kg Pu^{238}
- Final wiring and connections for ASRG engineering unit underway
- Reliability to be demonstrated by the end of 2009

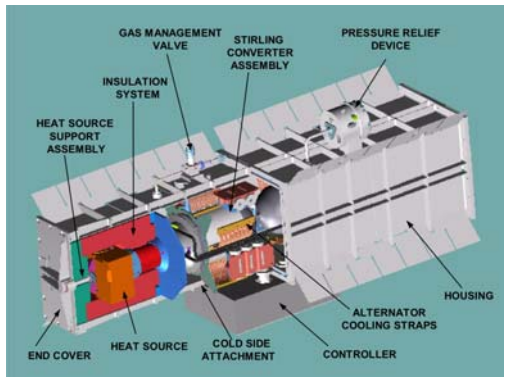

Lockheed Martin/Sunpower

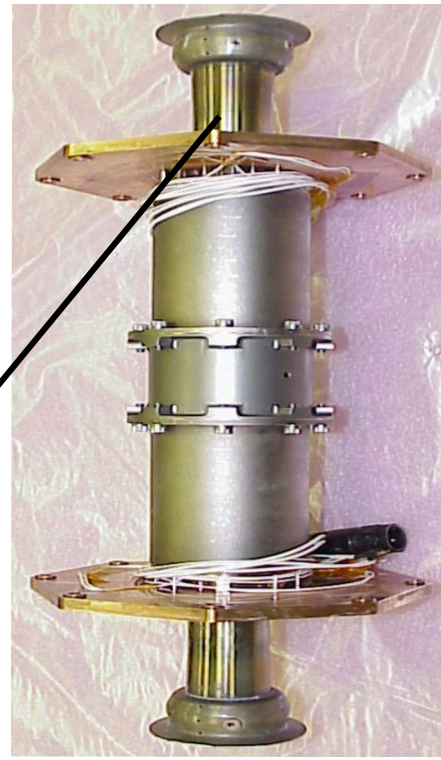

Paired converters with interconnect sleeve assembly

Outboard Housing and Paired ASC-Es

Long-lived Power Supplies

Short title of recommendation

- Develop long-lived power supplies for planetary missions

Brief Description of Recommendation:

- Take steps to develop or ensure the availability of long-lived power supplies for landed networks and other planetary missions.

Future Work

- Review NASA responses to selected NAC recommendations arising from the Tempe Lunar Science Workshop in the July meeting

- E/PO will be on the SC agenda for July
  - Will invite Human Capital Committee participation
